

東亞交匯一號海纜系統 (EAC1) 區段 D 海纜故障維修作業範圍略圖

- EAC1-D Cable Network Route Map (Taiwan)**

**EAC1 Submarine Cable System (Taiwan)**

  - EAC I Seg. A Submarine Cable
  - EAC I Seg. B Submarine Cable
  - EAC I Seg. C Submarine Cable
  - **EAC I Seg. D Submarine Cable**
  - EAC I Seg. E Submarine Cable

— The Outer Limits of the Contiguous Zone of R.O.C. (24 NM from Baseline)


— The Outer Limits of the Territorial Sea of R.O.C. (12 NM from Baseline)

**EAC1區段D海纜故障維修作業範圍略圖：**

  - A. 23° 46.4160' N、122° 15.4102' E
  - B. 23° 58.0400' N、122° 17.8040' E
  - C. 24° 06.5160' N、122° 30.1667' E
  - D. 24° 16.8572' N、122° 30.5663' E
  - E. 24° 15.3109' N、122° 38.7211' E
  - F. 24° 07.8221' N、122° 39.8923' E
  - G. 23° 59.4431' N、122° 35.8309' E
  - H. 23° 53.7083' N、122° 26.0349' E
  - I. 23° 37.3485' N、122° 25.2635' E
  - J. 23° 37.3904' N、122° 17.1499' E



堅定號（CS RESOLUTE）執行 EAC1 區段 D 海纜故障維修作業區域圖

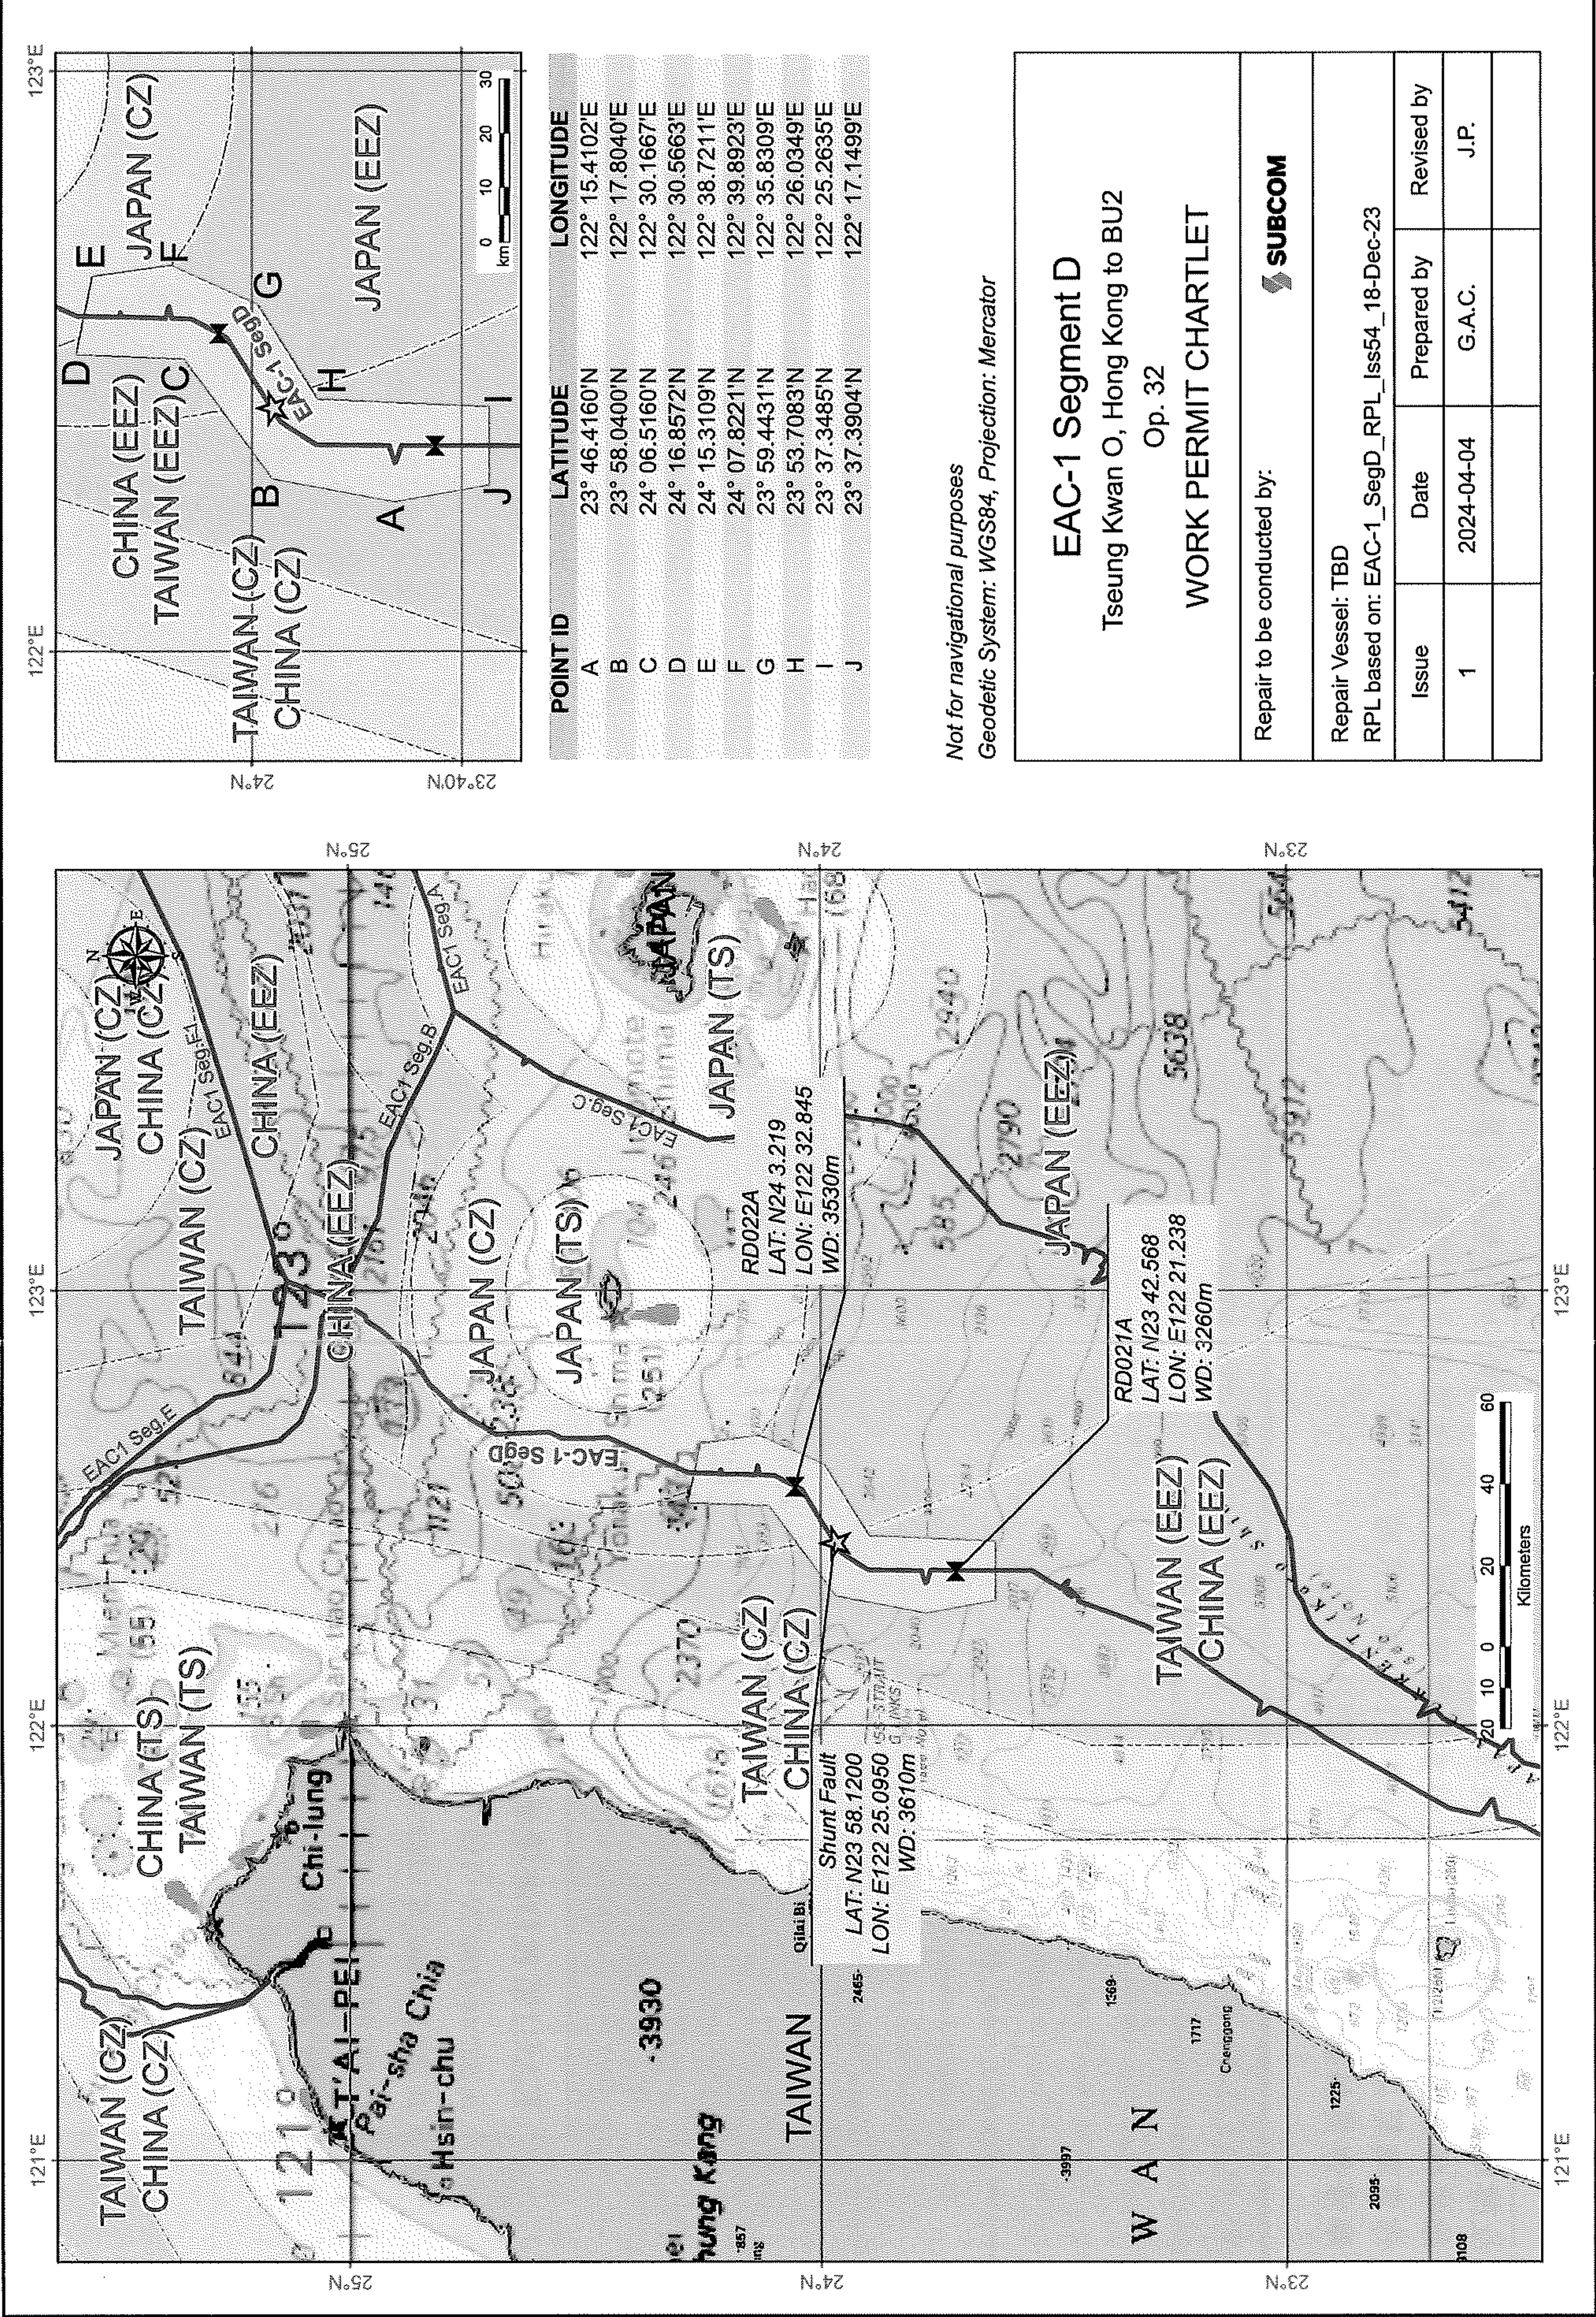



附件二：東亞交匯一號海纜系統（EAC1）區段 D 故障搶修時間表（含時間、作業內容）

作業海域：花蓮東部外海

作業船舶：堅定號（CS RESOLUTE）

編號	作業時間	作業內容
1	2024/04/10 ~ 2024/04/13	前往台中港。
2	2024/04/14 ~ 2024/04/16	台中港內海纜維修作業前準備工作。
3	2024/04/21	前維修海域。
4	2024/04/22	到達維修海域；進行故障位置搜尋與確認工作；撈鉤與海纜切斷作業。
5	2024/04/23 ~ 2024/04/25	撈起第一端海纜；測試作業；確認海纜障礙位置；海纜末端處理、準備海纜初始接續作業。
6	2024/04/26	海纜初始接續與測試作業。
7	2024/04/27 2024/04/28	接續後海纜佈放作業；海纜末端處理、準備海纜最終接續作業。
8	2024/04/29 ~ 2024/04/30	海纜最終接續與測試作業。
9	2024/05/01 ~ 2024/05/02	維修後海纜重新佈放作業。
10	2024/05/03 ~ 2024/05/05	海事備用時間。
12	2024/05/06	離開維修海域；維修任務結束。

備註：  
上列作業時間及作業內容供參考（實際作業期間將隨故障情況、修理進度、當時海象及新冠肺炎疫情狀況而調整）



### 附件三：堅定號(CS RESOLUTE)海纜船船舶照片及規格資料

主要規格：140 m（長） 21 m（寬） 12.6 m（深） 12,184 ton（總噸位） 3,655 ton（淨噸位）

船 級：特殊儀裝佈纜船（Cable Ship） 國 籍：馬紹爾群島籍（Marshall Island）

AIS 系統：MMSI No. 538001923 & IMO No. 9242340 船 呼（Call Sign）：V7FF3

